

CONSTRUCTION ERP

User Manual

Web Portal · Admin Panel · Mobile App

Step-by-step project flow and complete screen guide with actual screen captures

Version 1.0 · Construction Project Tracking System

React + Vite portals · Express + MySQL API · React Native (Expo) app

Contents

Contents	2
1. About the system	3
2. Roles and who does what	3
3. Getting access & first login	4
4. The project flow — step by step	5
5. Web Portal — screen guide	7
6. Admin Panel — screen guide	26
7. Mobile App — screen guide	34
8. A day in the life, by role	35
9. Status & workflow reference	35
10. Tips, FAQ & troubleshooting	36

1. About the system

Construction ERP tracks everything that happens on a construction site — from daily progress photos and worker attendance to materials, quality checks, costs and unit sales — in one place. It has three user-facing applications plus a backend:

App	Who uses it	Where
Web Portal (web-app)	Project managers, engineers (civil/electrical/plumbing), store manager, sales team, accountants, safety & quality officers	Browser — laptop, tablet or phone
Admin Panel (admin-panel)	Super Admin / Admin	Browser
Mobile App (mobile)	Site engineers & site staff on the field	Android / iOS via Expo Go or a store build

Key ideas to know before you start:

- **Structure** — every project is broken into **Projects** → **Wings/Blocks/Towers** → **Floors** → **Units**. Progress rolls up automatically (floor % → wing % → project %).
- **Permissions** — you only see the modules your role allows, and only the **projects/wings you are assigned to**. Buttons for actions you're not allowed to do are hidden (and blocked server-side anyway).
- **Offline-first mobile capture** — progress reports and issues can be saved without network; they sync automatically later, without duplicates.
- **Everything is audited** — every create/edit/delete records who did it, when, and what changed.

2. Roles and who does what

The system ships with 12 ready-made roles. Admins can also create **custom roles** with any permission mix (see §6.3).


Role	What they do daily
Super Admin	Full control: users, roles, all projects, all data, admin panel.
Admin	Same as Super Admin except cannot manage roles' permission matrix internals.
Project Manager (PM)	Owens their projects: structure, plans, milestones, approvals (requirements, BOQ), all reports, issues, billing, workforce.
Site Engineer	Daily progress reports with GPS photos, attendance marking, issues, inspections, material consumption entries — only on assigned projects/wings.
Civil / Electrical / Plumbing Engineer	Same as Site Engineer, scoped to their discipline's projects/wings (demo accounts are wing-scoped as examples).
Store Manager	Materials master, requirements → PO → GRN → stock, suppliers, consumption validation, low-stock alerts.
Quality Engineer	Test reports (upload lab results, approve/reject), inspections with checklists.
Safety Officer	Inspections, safety issues, documents.
Sales Executive	Unit sales, booking-to-payment tracking, collections.
Accountant	Billing & cost entries, vendor payments, labour payments, sales payments, financial reports.

Role	What they do daily
Custom roles	Anything you define — e.g. "Contractor (view-only)", "Client (view-only)", "Surveyor".

8 permission actions per module: [view](#) · [create](#) · [edit](#) · [delete](#) · [approve](#) · [export](#) · [upload](#) · [download](#).

3. Getting access & first login

3.1 Log in

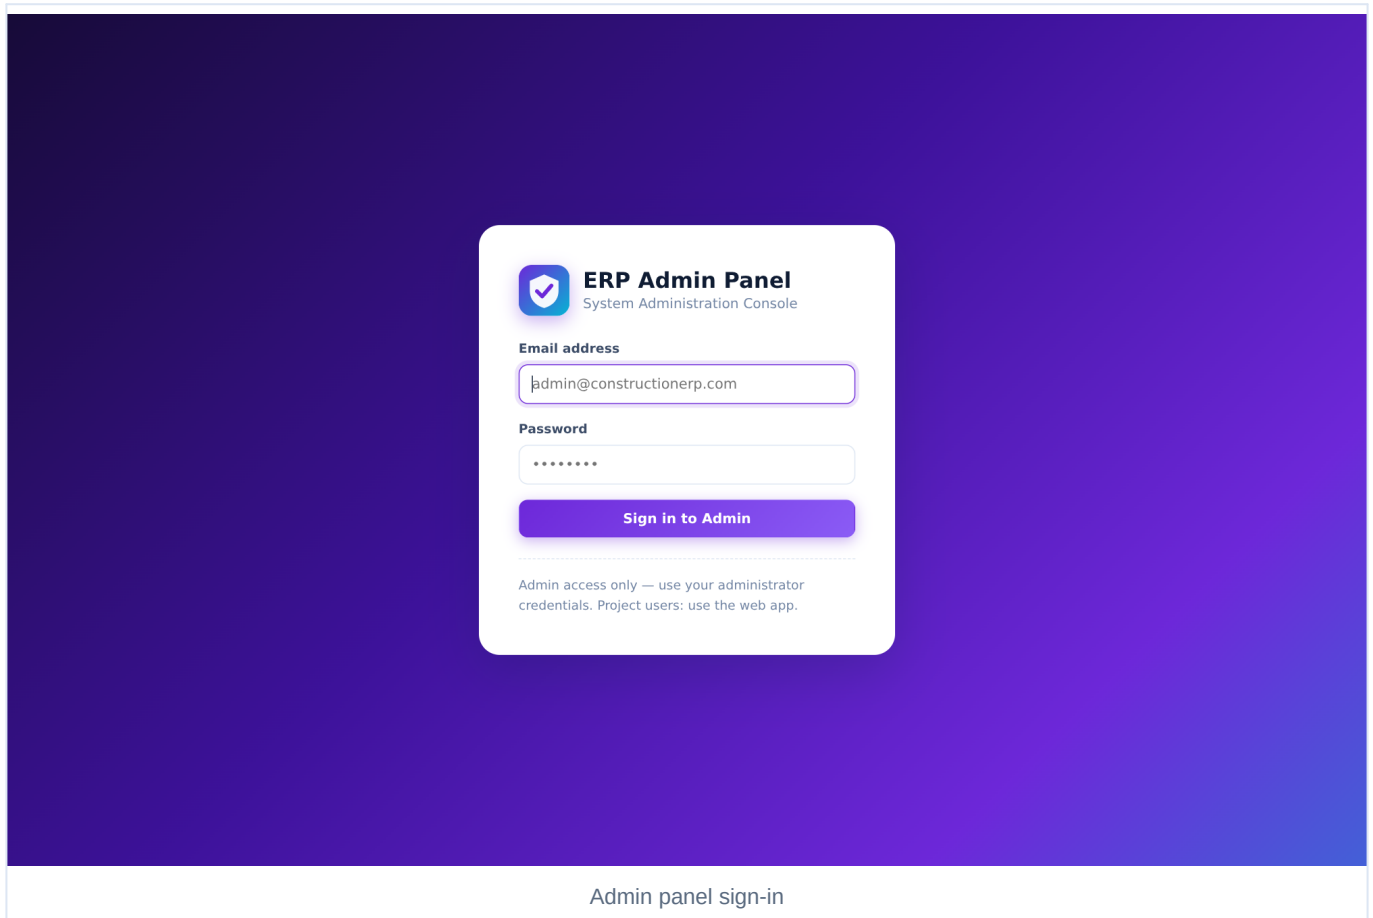

Admin panel sign-in

1. Open the **Web Portal** URL (e.g. <http://your-server:5173>) — mobile app: open the app.
2. Enter your **email** and **password**, press **Sign in**.
3. First time? Your admin will share your credentials. The seeded super admin is admin@constructionerp.com / [Admin@123](#) (change it immediately in production).


Forgot password — tap **Forgot password?** on the login screen, enter your email, and use the reset link (valid 30 minutes) to set a new one on the Reset Password page.

3.2 Set up your profile

Top-right user chip → **My Profile**:

- Update name, phone, profile details.
- **Change password** — enter current password, then the new one. Active sessions are revoked on password change.

3.3 The shell (web)

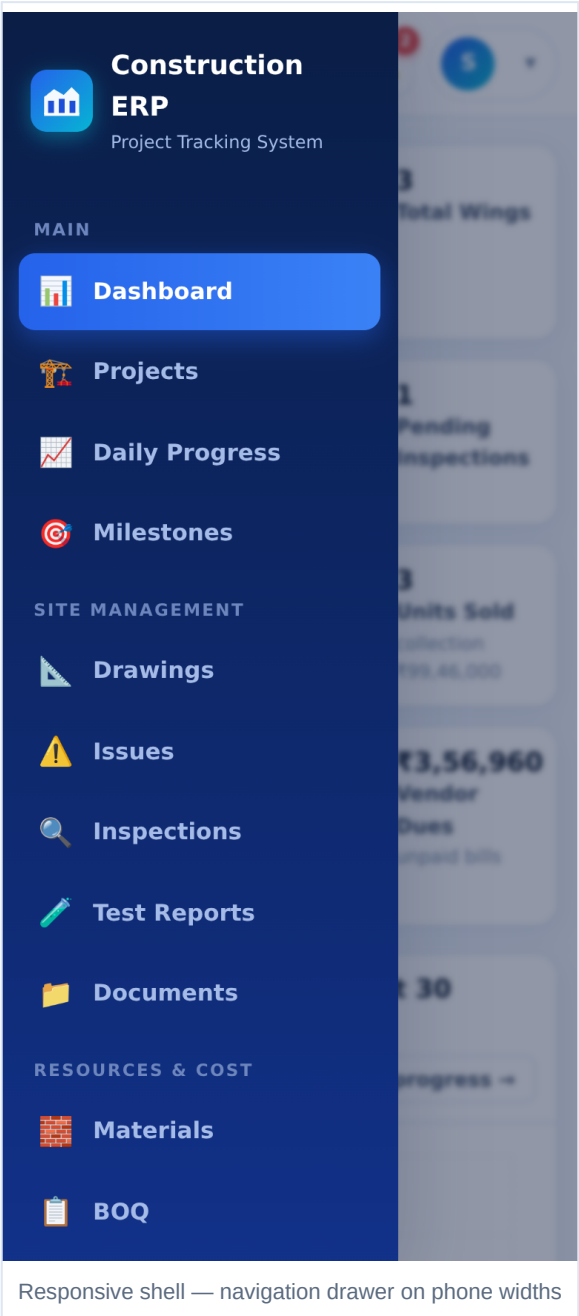

Responsive shell — navigation drawer on phone widths

Area	Purpose
Sidebar (left)	Module navigation, grouped: Main · Site Management · Resources & Cost · Insights. On phones it's hidden — tap ■; it slides in over a dimmed backdrop.
Top bar	Page title, ■ notifications bell (unread count badge, tap to open latest, "Mark all read"), and your user menu (profile / logout).
Content	Cards, tables, filters. Tables scroll sideways on small screens; every list has column filters, search and pagination.

4. The project flow — step by step

This is the complete lifecycle of a project in the system, end to end. Each step names **who** does it and **where** (Web / Admin / Mobile).

Phase 0 — Foundation setup (*Super Admin / Admin · Admin Panel*)

1. **Create the users** — Admin Panel → **Users** → **+ New User**: name, email, employee code, phone, initial password.
2. **Assign roles** — in the same user dialog, toggle roles (e.g. "Site Engineer"). Multiple roles are allowed.
3. **Create the project** — Web Portal → **Projects** → **+ New Project**: name, code, client, city/address, type, **budget**, start/target dates. (PM can also do this.)
4. **Grant project access** — Admin Panel → **Users** → edit user → **Project Access**: add project, optionally restricted to one **wing**. Users only see what's assigned to them (*Super Admin/Admin/PM see their managed projects*).
5. **Review master data** — Admin Panel → **Masters**: check material categories, worker categories, labour rates, contractors, BOQ categories, test types, inspection types, issue categories, notification settings. Add your own — these feed every dropdown in the system.

Phase 1 — Build the project structure (PM / Site Engineer · Web Portal)

1. Open **Projects** → click your project → **Structure** tab.
2. **Add Wings/Blocks/Towers** — e.g. "Wing A", code **A**.
3. Select a wing → **add Floors** — e.g. "Floor 1"… (with sequence numbers).
4. Select a floor → **add Units** — unit number (e.g. **A101**), carpet area (sq.ft), price. Units drive the Sales module.
5. Switch to the **Wings** tab to track wing status (planning → in_progress → completed) as work proceeds.

Phase 2 — Plan (PM · Web Portal)

1. **Milestones** — create the big checkpoints ("Foundation complete", "7th slab", "MEP first fix") with start/target dates and a responsible person. Progress % updates automatically flip milestones to *delayed* if the target date passes.
2. (Optional) **BOQ** — open **BOQ** → **+ New BOQ**, add line items (work description, unit, estimated quantity, rate). The system computes **estimated amount = qty × rate** and later compares actuals for variance %. You can also **import a whole BOQ from CSV/Excel paste** and **export** templates.
3. (Optional) **Drawings** — upload the first issue of drawings (PDF/JPG/PNG) with drawing number and discipline.

Phase 3 — Daily site execution (Site Engineers · Mobile App or Web)

Every day on site:

1. **Mark attendance** — Mobile → **Attendance**: pick project/wing/date, tap each worker → *Present / Absent / Leave / Half-day*, add OT hours where needed → **Save**. Daily wage and overtime cost are computed automatically.
2. **Capture daily progress** — Mobile → **Progress** → ■: take **photos** (the app attaches **GPS coordinates + timestamp**), describe work done, enter %, labour count, materials used → **Submit**. Works fully **offline** — entries queue and sync when the network is back (no duplicates). Web users can do the same at **Daily Progress** → **+ New Report**.
3. **Raise issues immediately** — anything unsafe, blocking or defective: Mobile/Web **Issues** → ■: photo(s) + GPS, title, category, priority (low→critical), due date, optionally assign to a teammate. The assignee gets a **notification**.
4. **Record material consumption** — Web → **Materials** → **Consumption** → **+ New**: material, quantity, wing/floor, location. Stock is checked live — you can't consume more than available.

Phase 4 — Materials cycle (Store Manager / PM · Web Portal)

1. **Requirement raised** — Materials → **Requirements** → **+ New**: material, quantity, needed-by date, remarks. PM sees and **approves/rejects** it.
2. **Purchase Order** — **Purchase Orders** → **+ New PO**: supplier, line items (material × qty × rate), tax %, discount %. Totals (subtotal + tax – discount → **grand total**) are calculated automatically. Status moves: *draft* → *sent* → *partially_received* → *completed*.
3. **Goods Receipt (GRN)** — when material arrives: **Receipts (GRN)** → **+ New**: pick the PO, enter received & **damaged** quantities per item. Accepted quantity enters stock; damaged is recorded separately.
4. **Stock & alerts** — **Stock & Alerts** tab shows live stock per material from all movements (opening + receipts – consumption – damage – returns). Anything at/below its **minimum level** shows in the low-stock alert list and on the dashboard.

5. **Returns** — **Consumption** overflow or damaged stock → record a **Material Return**; once approved it posts to the ledger.

Phase 5 — Quality gates (*Quality Engineer / Safety · Web + Mobile*)

1. **Material tests** — Quality → **Test Reports** → + **New**: test type (cube strength, steel tensile...), material, sample/test dates, laboratory, result values, upload the lab report PDF. Mark **pass/fail**; approvers can review and confirm.
2. **Stage inspections** — Quality → **Inspections** → + **New** (or Mobile → **Inspections**): inspection type (pre-slab checklist, rebar check, waterproofing...), project/wing/floor/location, date, and **check each checklist item pass / fail / N/A** with remarks. Attach photos + GPS. Failed inspections go to *reinspection_required*.
3. Issues found during inspections are raised as **Issues** and tracked to closure.

Phase 6 — Workforce money (*Accountant · Web Portal*)

1. **Generate labour payments** — Workforce → **Payments** → **Generate from Attendance**: pick worker + period; the system computes payable = Σ daily amounts + OT from attendance registers, you add deductions/adjustments → create the payment record.
2. **Track & pay** — payments show *pending/partial/paid*; record paid amount, date, mode and reference when disbursed.

Phase 7 — Billing & cost control (*Accountant / PM/ · Web Portal*)

1. **Book costs** — **Billing** → + **New Cost Entry**: category (labour/material/equipment/...) , vendor, invoice no., amount + tax, paid amount. Status tracks *unpaid/partial/paid*.
2. **Watch budget vs actual** — the dashboard cards and the **Budget vs Actual** report compare the project budget with cumulative cost live.

Phase 8 — Sales & collections (*Sales Team · Web Portal*)


1. **Sell a unit** — **Sales** → + **New Sale**: project → wing → floor → **unit** (only available units list), customer name/phone, booking & sale dates, sale amount, GST. Unit status flips to *sold/booked* and disappears from availability.
2. **Record payments** — open the sale → **Add Payment**: amount, date, mode, reference. Status flows *pending* → *partially_paid* → *paid* (overdue shows if the schedule passes).
3. **Collections view** — sales summary cards: sold units, value, received, pending; the **Pending Collections** report lists what to chase.

Phase 9 — Track, report, close (*Everyone*)

1. **Dashboard** every morning: KPIs (projects, progress %, open issues, low stock, today's attendance), 30-day progress trend, budget vs actual, pending approvals.
2. **Reports** module: 16 ready reports — project/daily progress, milestones, stock, consumption, POs, billing, BOQ, test reports, inspections, issues, attendance, sales, budget-vs-actual, pending collections, labour payments — view on screen or **download CSV**, date-filter and print.
3. **Close out** — mark milestones completed, close issues, finish drawings revisions, complete POs; set wings then project status to **completed**.

5. Web Portal — screen guide

5.1 Login / Forgot / Reset Password

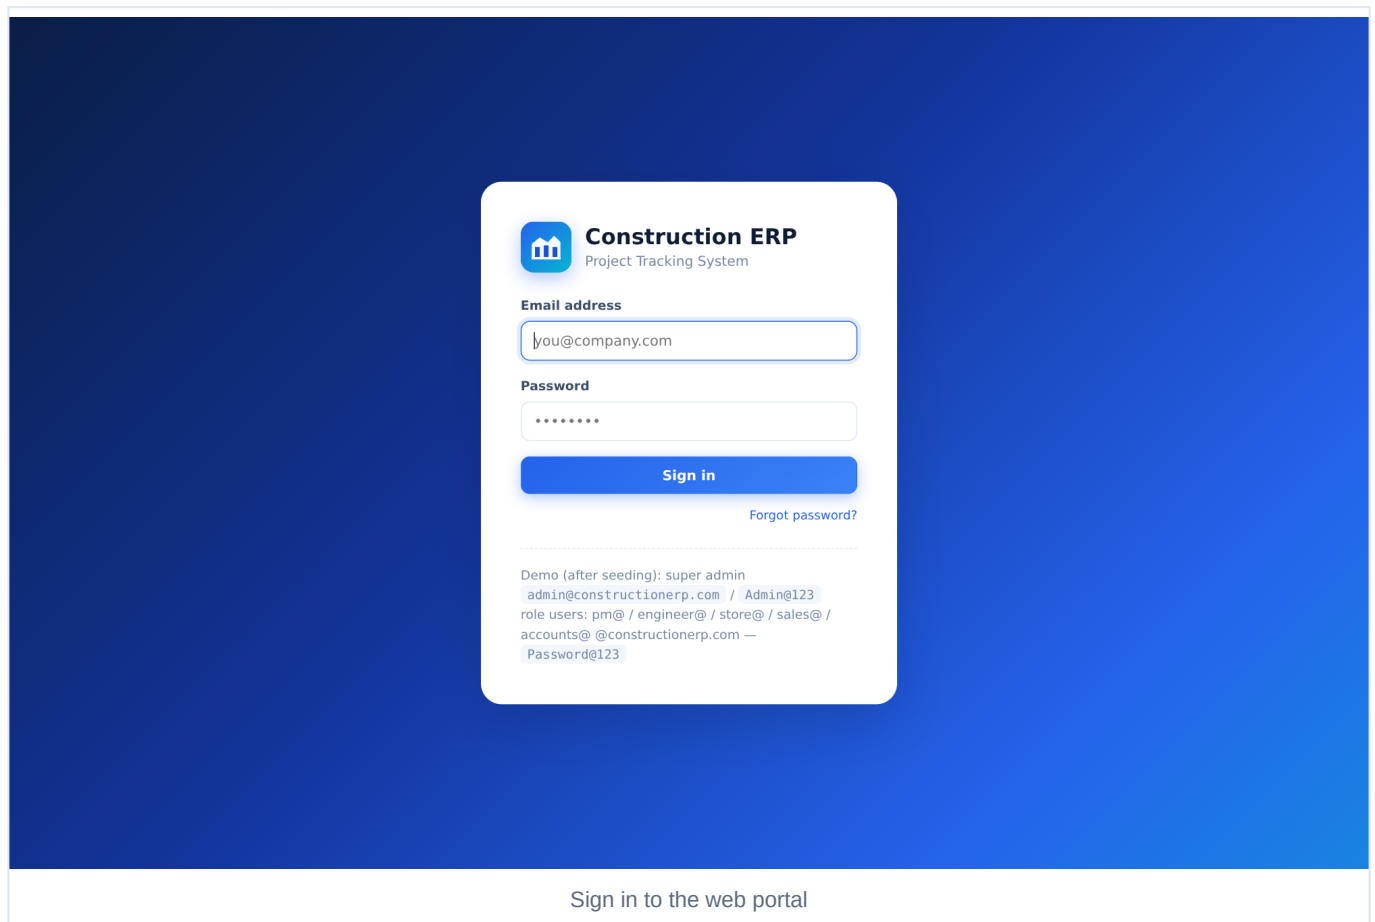

The image shows a login interface for 'Construction ERP Project Tracking System'. It features a dark blue gradient background. In the center is a white rounded rectangle containing the login form. The form has a logo at the top left, followed by the title 'Construction ERP' and subtitle 'Project Tracking System'. Below this are two input fields: 'Email address' with the placeholder 'you@company.com' and 'Password' with masked characters. A blue 'Sign in' button is positioned below the password field. To the right of the button is a link 'Forgot password?'. At the bottom of the white box, there is a section for demo credentials: 'Demo (after seeding): super admin', 'admin@constructionerp.com / Admin@123', and a list of roles: 'role users: pm@ / engineer@ / store@ / sales@ / accounts@ @constructionerp.com — Password@123'. Below the white box, a light blue bar contains the text 'Sign in to the web portal'.

Construction ERP
Project Tracking System

Email address
you@company.com

Password

Sign in


[Forgot password?](#)


Demo (after seeding): super admin
admin@constructionerp.com / Admin@123
role users: pm@ / engineer@ / store@ / sales@ /
accounts@ @constructionerp.com —
Password@123

Sign in to the web portal

Split-screen blue gradient login. Enter email + password → Sign in. **Forgot password** sends a reset link; **Reset Password** sets a new password from that link.

5.2 Dashboard

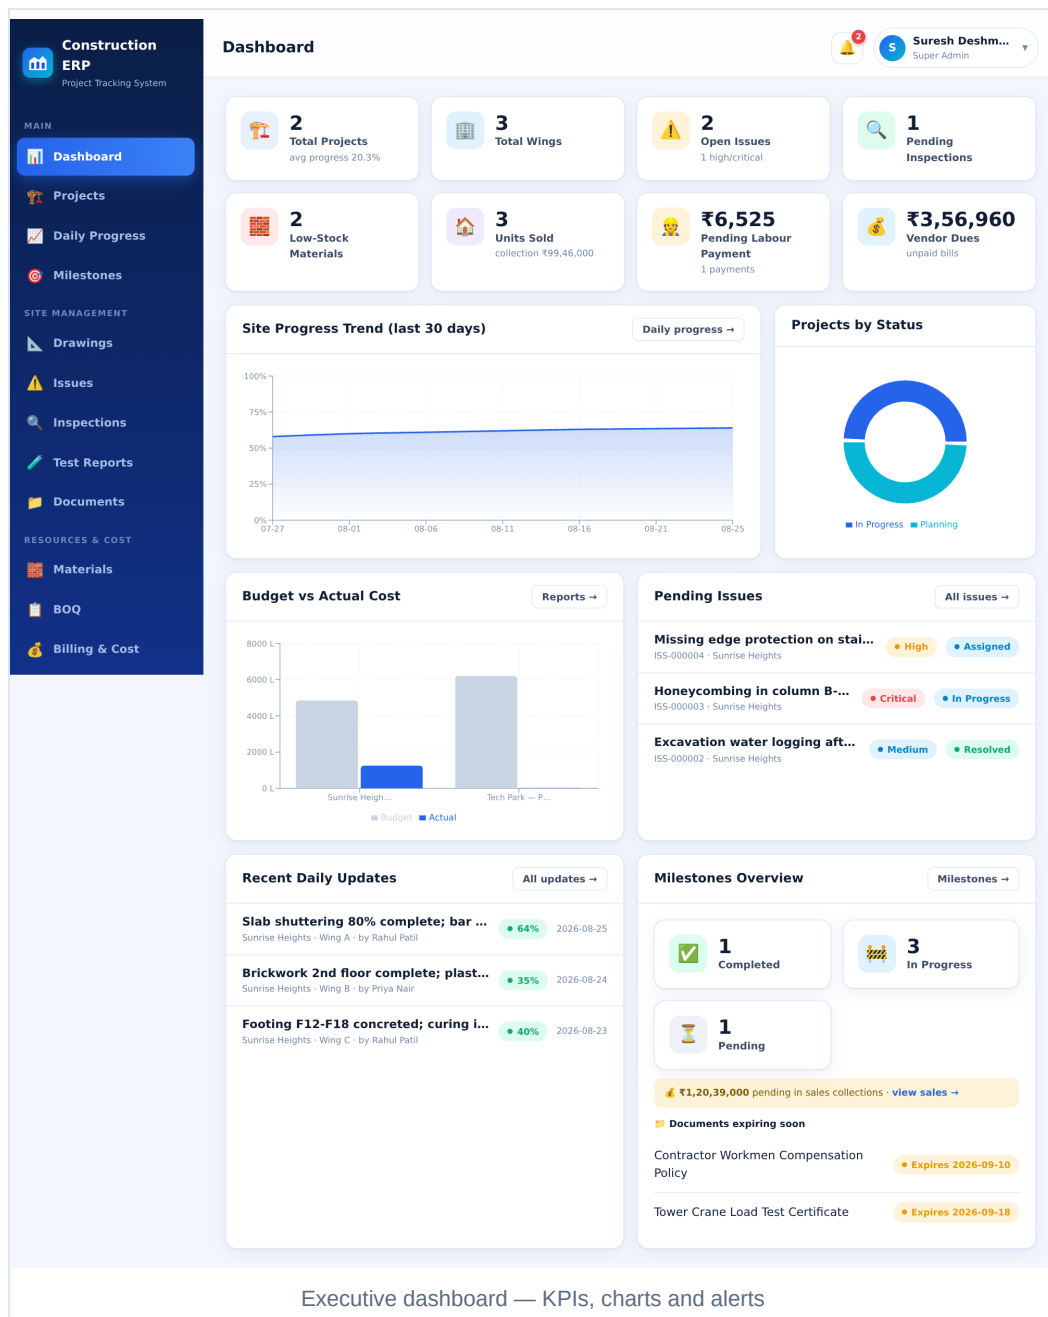

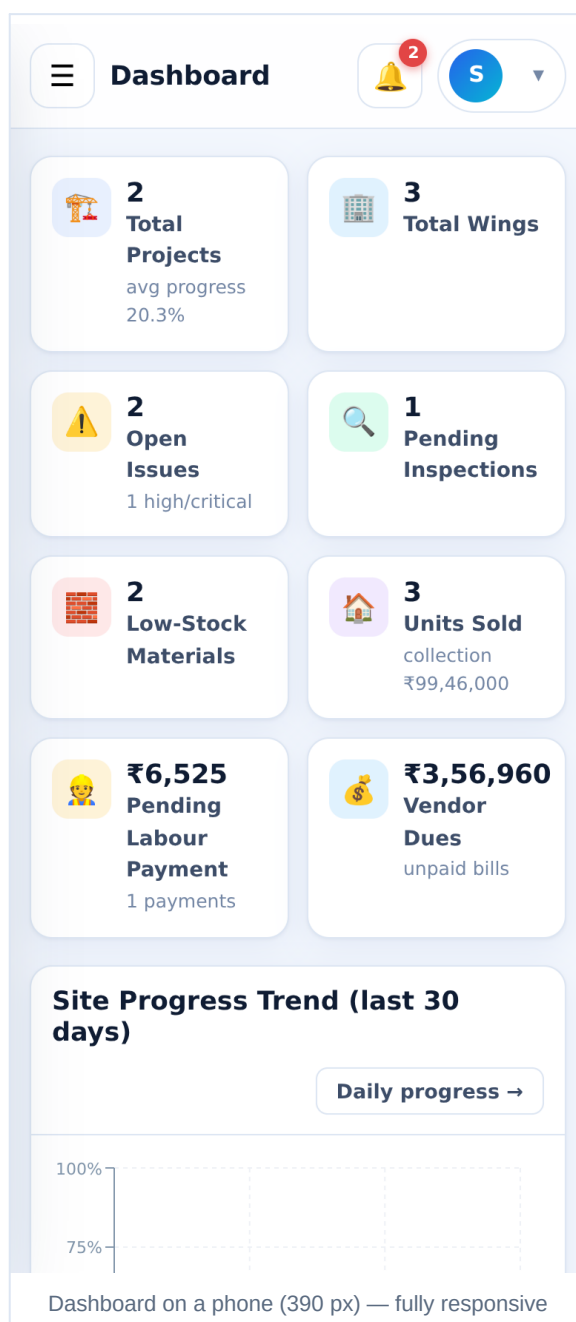

Your home: KPI cards (Projects with avg progress, Wings, Open Issues with high/critical count, Pending Inspections, Low-Stock Materials, Units Sold + collections, Pending Labour Payments, Vendor Dues), a **30-day progress trend** area chart, **Budget vs Actual** per project bars, project status donut, milestone status strip, plus lists: recent progress reports, open issues by priority, documents expiring in 30 days.

5.3 Projects



Construction ERP

Project Tracking System

MAIN

 Dashboard

 Projects

 Daily Progress

 Milestones

SITE MANAGEMENT

 Drawings

 Issues

 Inspections

 Test Reports

 Documents

RESOURCES & COST

 Materials

 BOQ

 Billing & Cost

Projects

 Export CSV

 New Project

Search

Search name, code, client, city...

Status

All

Type

All

CODE	PROJECT	TYPE	CLIENT	MANAGER	WINGS	BUDGET	PROGRESS	STATUS
PRJ - 000001	Sunrise Heights Nagpur	Residential High-Rise	Skyline Developers LLP	Amit Verma	—	₹48,50,00,000	38%	In Progress
PRJ - 000002	Tech Park — Phase 2 Nagpur	Commercial	InfoSpace Realty	Amit Verma	—	₹62,00,00,000	2%	Planning

2 records · page 1 of 1

PrevNext

Projects list with progress bars and budgets



Construction ERP

Project Tracking System

MAIN

 Dashboard

 Projects

 Daily Progress

 Milestones

SITE MANAGEMENT

 Drawings

 Issues

 Inspections

 Test Reports

 Documents

RESOURCES & COST

 Materials

 BOQ

 Billing & Cost

Project Details

 Export CSV

 New Project

Sunrise Heights

In ProgressResidential High-Rise

PRJ - 000001 · Skyline Developers LLP · Nagpur · Manager: Amit Verma

Start: 2025-03-01

Due: —

Budget: ₹48,50,00,000

Overall progress

38%

Overview

Wings (3)

Progress Timeline

Floors & Units

Developer

—

Address

Plot 42, Wardha Road, Nagpur

Description

—

Budget

₹48,50,00,000

Actual cost

₹10,13,960 (0.21% of budget)

Paid / Pending

₹6,57,000 / ₹3,56,960

Project details — overview, wings, timeline, floors & units

Filter by status/type, search. + **New Project** (name, code, client, city, address, type, budget, dates, manager). Click a row → Project Detail:

- **Overview** — KPIs, progress bar, key facts, budget vs cost.
- **Wings** — add/edit wings with progress bars & statuses; per-wing **Wing Dashboard** shows floor progress, inspection results pie, material status, recent progress.
- **Structure** — wings → floors → units tree with add/edit/delete and unit pricing.
- **Progress** — timeline of that project's daily reports with photos.

5.4 Daily Progress

Construction ERP
Project Tracking System

MAIN

- Dashboard
- Projects
- Daily Progress**
- Milestones

SITE MANAGEMENT

- Drawings
- Issues
- Inspections
- Test Reports
- Documents

RESOURCES & COST

- Materials
- BOQ
- Billing & Cost

Daily Progress

Daily Progress Reports

Export New Report

Search Project Wing

Search descriptions... All projects All wings

DATE	WORK	PROGRESS	LABOUR	PHOTOS	GPS	BY
2026-08-25	Slab shuttering 80% complete; bar ... Sunrise Heights - Wing A - Floor 7	64%	38	2	map	Rahul Patil
2026-08-24	Brickwork 2nd floor complete; plast... Sunrise Heights - Wing B - Floor 3	35%	26	1	map	Priya Nair
2026-08-23	Footing F12-F18 concreted; curing i... Sunrise Heights - Wing C	40%	22	1	map	Rahul Patil

3 records · page 1 of 1 Prev Next

Daily progress reports with photos and GPS

All reports, newest first: date, project/wing/floor, description, %, labour, weather, GPS **map links**, photo thumbnails (authenticated image viewer). + **New Report**: pick project (wing/floor cascade), date/time, work description, % completed, labour count, materials used, weather, remarks, attach photos — each photo keeps latitude/longitude/timestamp/uploader. Web page also keeps an **offline queue** (saved in the browser) if the network drops. Export CSV available.

5.5 Milestones



Construction ERP

Project Tracking System

MAIN

 Dashboard

 Projects

 Daily Progress

 Milestones

SITE MANAGEMENT

 Drawings

 Issues

 Inspections

 Test Reports

 Documents

RESOURCES & COST

 Materials

 BOQ

 Billing & Cost

Milestones



2

S

Suresh Deshm...

Super Admin

Milestones

+ New Milestone

Search

Project

Status

Search...

All

All

MILESTONE	START	TARGET	PROGRESS	STATUS	RESPONSIBLE		
Foundation & Plinth Completion Sunrise Heights - Wing A	2025-05-01	2025-08-31	100%	Completed	Rahul Patil	Edit	Delete
Superstructure — Slabs up to 7th Sunrise Heights - Wing A	2025-09-01	2026-02-28	62%	In Progress	Rahul Patil	Edit	Delete
Brickwork & Plaster Sunrise Heights - Wing B	2025-11-01	2026-05-31	35%	In Progress	Priya Nair	Edit	Delete
Foundation Completion Sunrise Heights - Wing C	2026-01-01	2026-04-30	40%	In Progress	Rahul Patil	Edit	Delete
MEP First Fix Sunrise Heights	2026-06-01	2026-10-31	0%	Pending	Vikram Joshi	Edit	Delete

5 records · page 1 of 1

PrevNext

Milestones with progress and ownership

Table by project with target dates, % complete, status (pending/in_progress/completed/delayed — auto-flips to delayed past target date). + **New Milestone**: project, optional wing, name, dates, responsible user, %.

5.6 Drawings

Construction ERP v1.0 - Project Tracking System

Page 13

Construction ERP
Project Tracking System

MAIN

Dashboard
Projects
Daily Progress
Milestones

SITE MANAGEMENT

Drawings
Issues
Inspections
Test Reports
Documents

RESOURCES & COST
Materials
BOQ
Billing & Cost

Drawings

Suresh Deshm...
Super Admin

Drawings & Document Control

+ Upload Drawing

Search
Drawing number or title...

Project
All

Category
All

DRAWING NO.	TITLE	CATEGORY	REV	STATUS	UPLOADED BY
SH-A-ST-101	Foundation Layout Plan — Wing A Sunrise Heights · Wing A	• Structural	• R2	• Approved	Vikram Joshi
SH-A-ST-201	Typical Floor Framing — Wing A Sunrise Heights · Wing A	• Structural	• R1	• Approved	Vikram Joshi
SH-B-AR-102	Unit Plan Types A/B — Wing B Sunrise Heights · Wing B	• Architectural	• R2	• Pending Approval	Vikram Joshi

3 records · page 1 of 1

< Prev
Next >

Drawing register with revisions and approval status

Drawing register: number, title, discipline, project/wing, current revision, status. Upload new drawings (PDF/JPG/PNG). Open a drawing → **revision history** — add a revision, **Approve / Reject** revisions, preview the file in-browser.

5.7 Materials (7 tabs)



Construction ERP

Project Tracking System

MAIN

 Dashboard

 Projects

 Daily Progress

 Milestones

SITE MANAGEMENT

 Drawings

 Issues

 Inspections

 Test Reports

 Documents

RESOURCES & COST

 Materials

 BOQ

 Billing & Cost

Materials & Inventory

 2

 Suresh Deshm...
Super Admin

Materials

Stock & Alerts

Requirements

Purchase Orders

Receipts (GRN)

Consumption

Suppliers

Materials

Export CSV

New

Search

Category

Search...

All

CODE	MATERIAL	CATEGORY	UNIT	MIN STOCK	STATUS		
STL-001	TMT Steel Fe500 12mm	Steel	kg	2,000	Active	Edit	Delete
CEM-001	Cement OPC 53 Grade	Cement	bag	150	Active	Edit	Delete
SAND-001	River Sand (Washed)	Aggregates	cft	500	Active	Edit	Delete
AGG-001	Aggregate 20mm	Aggregates	cft	400	Active	Edit	Delete
BLK-001	AAC Blocks 600x200x150	Masonry	nos	3,000	Active	Edit	Delete
PNT-001	Exterior Emulsion (White)	Finishing	ltr	100	Active	Edit	Delete

6 records · page 1 of 1

Prev

Next

Materials master



Construction ERP

Project Tracking System

MAIN

 Dashboard

 Projects

 Daily Progress

 Milestones

SITE MANAGEMENT

 Drawings

 Issues

 Inspections

 Test Reports

 Documents

RESOURCES & COST

 Materials

 BOQ

 Billing & Cost

Materials & Inventory

 2

 Suresh Deshm...
Super Admin

Materials

Stock & Alerts

Requirements

Purchase Orders

Receipts (GRN)

Consumption

Suppliers

Stock Position

Transactions

Refresh

Search

Project

Material name or code...

All

MATERIAL	PROJECT	RECEIVED	CONSUMED	DAMAGED	RETURNED	CURRENT STOCK	ALERT
TMT Steel Fe500 12mm STL-001	Sunrise Heights	29,000	21,200	0	0	7,800 kg	OK
Cement OPC 53 Grade CEM-001	Sunrise Heights	2,600	2,510	5	0	85 bag	OK
River Sand (Washed) SAND-001	Sunrise Heights	3,400	2,210	0	0	1,190 cft	OK
Aggregate 20mm AGG-001	Sunrise Heights	2,600	1,710	0	0	890 cft	OK
AAC Blocks 600x200x150 BLK-001	Sunrise Heights	26,000	23,300	0	0	2,700 nos	OK

Stock position with low-stock alerts



Construction ERP

Project Tracking System

MAIN

 Dashboard

 Projects

 Daily Progress

 Milestones

SITE MANAGEMENT

 Drawings

 Issues

 Inspections

 Test Reports

 Documents

RESOURCES & COST

 Materials

 BOQ

 Billing & Cost

Materials & Inventory



2

S

Suresh Deshm...

Super Admin

Materials

Stock & Alerts

Requirements

Purchase Orders

Receipts (GRN)

Consumption

Suppliers

Material Requirements

+ New

Search

Search...

Status

All

REQ NO.	MATERIAL	PROJECT	QTY	NEEDED BY	REQUESTED BY	STATUS				
	TMT Steel Fe500 12mm	Sunrise Heights Wing A	— kg	—	Rahul Patil	Approved	Edit	Delete		
	Cement OPC 53 Grade	Sunrise Heights	— bag	—	Priya Nair	Pending	Approve	Reject	Edit	Delete
	Aggregate 20mm	Sunrise Heights Wing C	— cft	—	Rahul Patil	Pending	Approve	Reject	Edit	Delete

3 records · page 1 of 1

Prev

Next

Material requirements with approve / reject



Construction ERP

Project Tracking System

MAIN

 Dashboard

 Projects

 Daily Progress

 Milestones

SITE MANAGEMENT

 Drawings

 Issues

 Inspections

 Test Reports

 Documents

RESOURCES & COST

 Materials

 BOQ

 Billing & Cost

Materials & Inventory



2

S

Suresh Deshm...

Super Admin

Materials

Stock & Alerts

Requirements

Purchase Orders

Receipts (GRN)

Consumption

Suppliers

Purchase Orders

+ New PO

Status

All

PO NO.	SUPPLIER	PROJECT	DATE	EXPECTED	TOTAL	STATUS
P0-000001	Mahalaxmi Steel Traders	Sunrise Heights	—	—	₹4,44,860	Partially Received
P0-000002	UltraBuild Cement Distributors	Sunrise Heights	—	—	₹1,60,650	Sent
P0-000003	Vidarbha Sand Suppliers	Sunrise Heights	—	—	₹1,00,800	Completed

3 records · page 1 of 1

Prev

Next

Purchase orders with receiving status

■ **Materials** — master list (name, code, category, unit, min stock). CRUD + CSV export.

Construction ERP v1.0 - Project Tracking System

Page 16

- **Stock & Alerts** — live stock per project from the stock-transaction ledger; low-stock alerts; full transaction history (receipt/consumption/damage/return).
- **Requirements** — requirement requests with PM **Approve/Reject** workflow (status: pending → approved → po_created / rejected).
- **Purchase Orders** — PO list + create with multi-line items, tax/discount, auto totals; open a PO for status transitions and to record receipts.
- **Receipts (GRN)** — receipts against POs with received/damaged quantities (posts stock transactions).
- **Consumption** — material consumed at wing/floor with live stock validation.
- **Suppliers** — supplier master with contact & GST details, CRUD + export.

5.8 BOQ


Construction ERP
 Project Tracking System

MAIN

Dashboard

Projects

Daily Progress

Milestones

SITE MANAGEMENT

Drawings

Issues

Inspections

Test Reports

Documents

RESOURCES & COST

Materials

BOQ

Billing & Cost

Bill of Quantities




Suresh Deshm...
 Super Admin

Bill of Quantities

Export CSV

New BOQ

Search

Search...

Status

All

BOQ NO.	TITLE	ESTIMATED	ACTUAL	VARIANCE	STATUS
BOQ-000001	Sunrise Heights — Civil Works BOQ Sunrise Heights	₹1,84,76,250	₹1,16,31,200	₹0	Active

1 record · page 1 of 1

Prev

Next

BOQ list

Construction ERP

Project Tracking System

MAIN

Dashboard

Projects

Daily Progress

Milestones

SITE MANAGEMENT

Drawings

Issues

Inspections

Test Reports

Documents

RESOURCES & COST

Materials

BOQ

Billing & Cost

Construction ERP

Suresh Deshm...
Super Admin

Sunrise Heights — Civil Works BOQ

Active

Export CSV

Add item

BOQ-000001 · Sunrise Heights

Estimated

Actual

Variance

Tax (%)

Grand Total


BOQ Items (4)

CODE	DESCRIPTION	UNIT	EST. QTY	RATE	EST. AMT	ACT. QTY	ACT. AMT	VAR %	
CW-01	M30 RCC for slabs & columns (supply + pour) Concrete	cum	1,850	₹7,150	₹1,32,27,500	812	₹58,05,800	—	Edit
CW-02	TMT Fe500 reinforcement — cut, bend, fix Steel	kg	42,000	₹68	₹28,56,000	21,200	₹14,41,600	—	Edit
CW-03	AAC block masonry 150mm thick Masonry	sqm	4,800	₹320	₹15,36,000	1,260	₹4,03,200	—	Edit
CW-04	12mm cement plaster internal, machine finish Plaster	sqm	9,600	₹185	₹8,55,000	1,986	₹6,67,600	—	Edit

BOQ detail — estimated vs actual with variance

BOQ list per project (title, items count, estimated vs actual). + **New BOQ**, or open one → detail: totals card (estimated total, actual total, cost variance %), items table with **qty × rate**, actual qty, **qty variance** and **cost variance** columns, add/edit items, **CSV template export + bulk import (paste CSV)**, export whole BOQ.

5.9 Billing & Cost

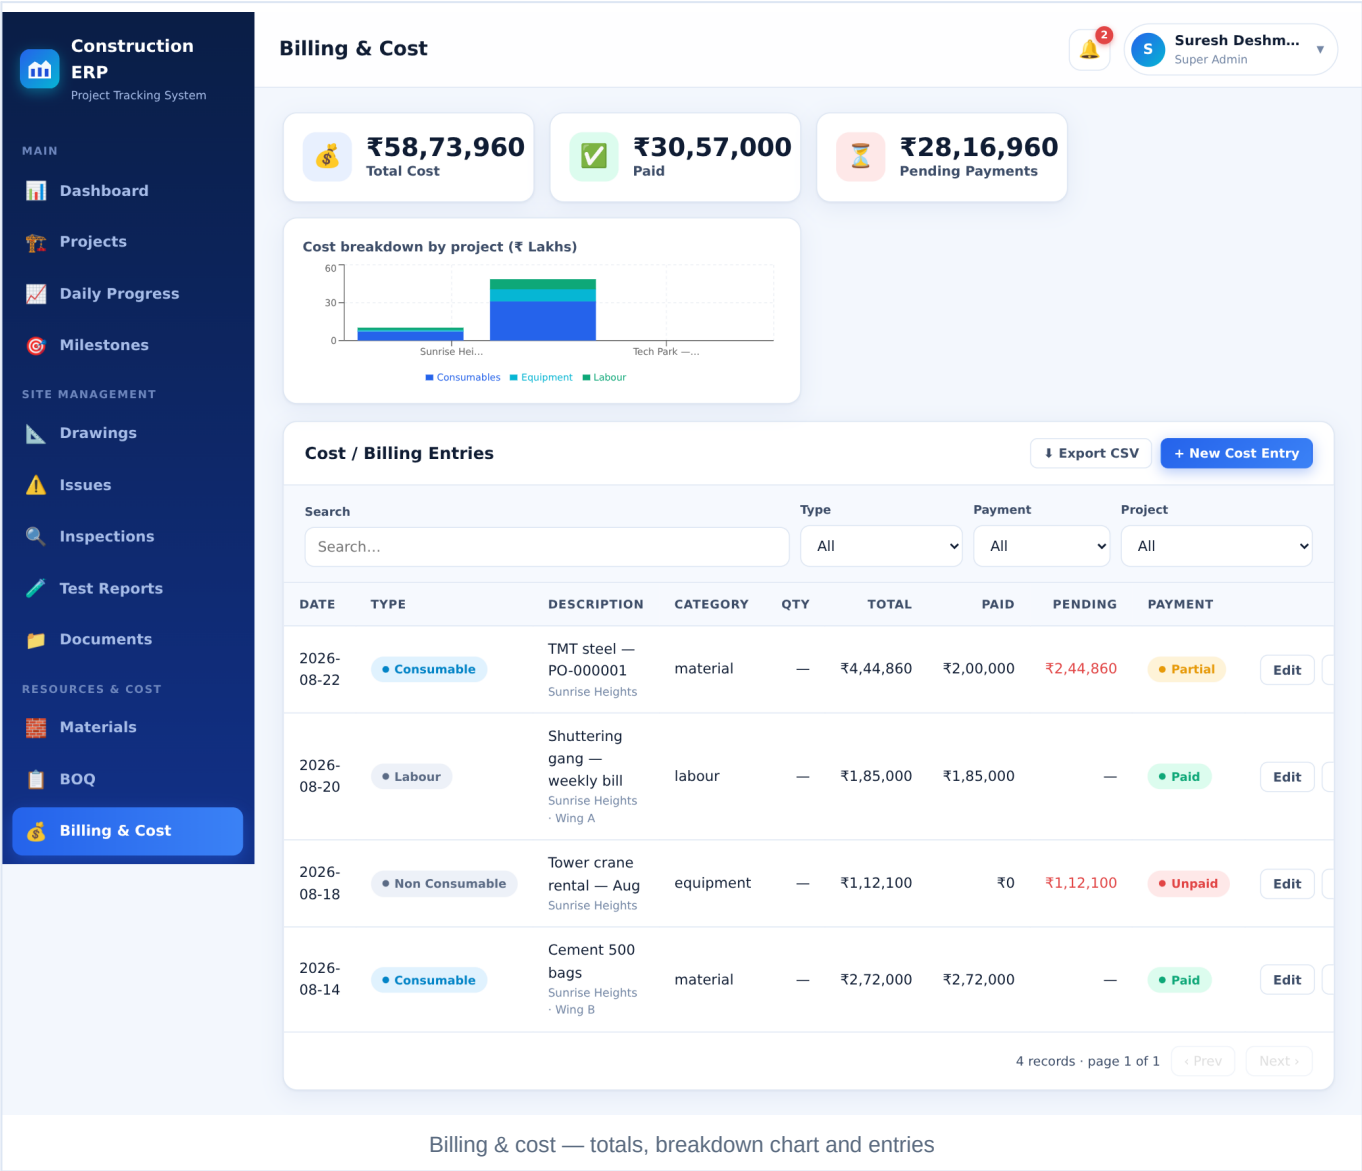

Stat cards (Total cost / Paid / Pending), stacked monthly cost chart, cost entries table (date, category, vendor, invoice, amount, tax, paid, status). + **New Cost Entry** — 20 fields incl. project/wing, category, vendor/supplier, amounts; payment status computes automatically from paid vs total.

5.10 Quality



Construction ERP

Project Tracking System

MAIN

Dashboard

Projects

Daily Progress

Milestones

SITE MANAGEMENT

Drawings

Issues

Inspections

Test Reports

Documents

RESOURCES & COST

Materials

BOQ

Billing & Cost

Test Reports



2

S

Suresh Deshm...

Super Admin

Test Reports

+ New Test Report

Search

Result

Test type

Search...

All

All

TEST NO.	TEST	PROJECT	MATERIAL	TEST DATE	LABORATORY	RESULT	STATUS	REPORT
TR-000003	Concrete Cube Compressive Strength	Sunrise Heights Wing A	M30 Design Mix	2026-08-25	SGBMaterials Lab, Nagpur	Pass	Approved	PDF Edit
TR-000002	Steel Tensile Strength	Sunrise Heights	TMT Steel Fe500 12mm	2026-08-21	SGS Nagpur	Pass	Approved	PDF Edit
TR-000001	Silt Content in Sand	Sunrise Heights	River Sand (Washed)	2026-08-13	In-house	Fail	Rejected	— Edit

3 records · page 1 of 1

Prev

Next

Material test reports with pass/fail results



Construction ERP

Project Tracking System

MAIN

Dashboard

Projects

Daily Progress

Milestones

SITE MANAGEMENT

Drawings

Issues

Inspections

Test Reports

Documents

RESOURCES & COST

Materials

BOQ

Billing & Cost

Inspections



2

S

Suresh Deshm...

Super Admin

Inspection Reports

+ New Inspection

Project

Status

All

All

NO.	TYPE	PROJECT	DATE	INSPECTOR	GPS	STATUS
INSP-000002	Pre-Slab Pour Checklist	Sunrise Heights Wing A · Wing A 6th slab	2026-08-23	Neha Desai		Passed
INSP-000001	Scaffolding Safety Inspection	Sunrise Heights Wing B · Wing B external scaffold	2026-08-21	Sunil Pawar		Reinspection Required

Close

Site inspections with checklists

Construction ERP v1.0 - Project Tracking System

Page 20

- **Test Reports** — table (test no., type, project, material, dates, lab, result **pending/pass/fail**, report file view).
Filters by type/result; approve/reject actions for authorized users.
- **Inspections** — list + create: type, project/wing/floor/location, date, observation, **checklist builder** (add items inline, each pass/fail/N/A + remarks), photos + GPS, status workflow pending → passed/failed/reinspection_required → closed.

5.11 Issues

Construction ERP
Project Tracking System

MAIN

Dashboard
Projects
Daily Progress
Milestones

SITE MANAGEMENT

Drawings
Issues
Inspections
Test Reports
Documents

RESOURCES & COST

Materials
BOQ
Billing & Cost

Issues

Suresh Deshm...
Super Admin

Site Issues

+ Raise Issue

Project
Status
Priority

All
All
All

NO.	ISSUE	CATEGORY	PRIORITY	STATUS	ASSIGNED TO	DUE
ISS-000004	Missing edge protection on stairwell opening Sunrise Heights · Wing A · Wing A, 5th floor stairwell	Safety	High	Assigned	Rahul Patil	2026-08-26
ISS-000003	Honeycombing in column B-G2 Sunrise Heights · Wing B · Wing B GF	Quality	Critical	In Progress	Rahul Patil	2026-08-24
ISS-000002	Excavation water logging after rain Sunrise Heights · Wing C · Wing C excavation	Schedule	Medium	Resolved	Sanjay Kale	2026-08-20
ISS-000001	Debris stacking near hoist Sunrise Heights · Wing A	Housekeeping	Low	Closed	—	—

4 records · page 1 of 1

Prev
Next

Site issues with priority, status and age

Filters (status, priority, category, project). + **New Issue** — title, category, priority, project/wing/floor, description, photos + GPS, assignee, due date. Open an issue → **status actions** (assign, start work, resolve, close, reopen) and the **comment thread**.

5.12 Workforce



Construction ERP

Project Tracking System

MAIN

 Dashboard

 Projects

 Daily Progress

 Milestones

SITE MANAGEMENT

 Drawings

 Issues

 Inspections

 Test Reports

 Documents

RESOURCES & COST

 Materials

 BOQ

 Billing & Cost

Workforce & Attendance

 2

S

Suresh Deshm...

Super Admin

Attendance

Workers

Labour Payments

Daily Attendance

Export

Project

Sunrise Heights

Date

08/25/2026

Pay Roll ₹3,230

Quick mark:

All present

All absent

Save attendance (5)

CODE	WORKER	STATUS					OT HRS	DAY PAY
WKR-001	Ramesh Yadav Mason · ₹950/day	present	absent	half day	leave	overtime	0	₹950
WKR-002	Santosh Kumar Bar Bender · ₹900/day	present	absent	half day	leave	overtime	2	₹1,130
WKR-003	Prakash Jadhav Carpenter · ₹1000/day	present	absent	half day	leave	overtime	0	₹500
WKR-004	Dinesh Wagh Helper · ₹650/day	present	absent	half day	leave	overtime	0	₹650
WKR-005	Mahesh Bhoyar Helper · ₹650/day	present	absent	half day	leave	overtime	0	—
WKR-006	Anil Gawande Electrician · ₹1050/day	present	absent	half day	leave	overtime	0	₹0

Daily attendance register



Construction ERP

Project Tracking System

MAIN

 Dashboard

 Projects

 Daily Progress

 Milestones

SITE MANAGEMENT

 Drawings

 Issues

 Inspections

 Test Reports

 Documents

RESOURCES & COST

 Materials

 BOQ

 Billing & Cost

Workforce & Attendance

 2

S

Suresh Deshm...

Super Admin

Attendance

Workers

Labour Payments

Labour Payments

 ₹6,525

Pending

+ Generate Payment

Project

All projects

WORKER	PERIOD	DAYS	OT HRS	NET	PAID	STATUS
Ramesh Yadav WKR-001	2026-08-01 → 2026-08-15	—	—	₹11,400	₹11,400	Paid
Santosh Kumar WKR-002	2026-08-01 → 2026-08-15	—	—	₹12,525	₹6,000	Partial

Mark paid

Labour payments with wages, advances and net payable

Construction ERP v1.0 - Project Tracking System

Page 22

- **Attendance** — date + project grid of all workers; quick-mark **All Present**, per-worker P/A/L/H/OT buttons with OT hours; live day total (Σ wages + OT); **Save** writes the whole day at once.
- **Workers** — worker master (code, name, category, contractor, daily wage, OT rate, phone).
- **Payments** — labour payment records; **Generate from Attendance** (worker + period → auto-computed payable), adjust deductions, record paid amounts/mode/reference; statuses pending → partial → paid; monthly register view.

5.13 Sales

Construction ERP
Project Tracking System

MAIN

Dashboard
Projects
Daily Progress
Milestones

SITE MANAGEMENT

Drawings
Issues
Inspections
Test Reports
Documents

RESOURCES & COST

Materials
BOQ
Billing & Cost

Sales

2

S
Suresh Deshm...
Super Admin

0
Units Sold
18 available

—
Sales Value

—
Collected

—
Pending Collections

Sales register
Export CSV

Unit Sales
+ New Sale

Search

Search...

Payment
All

GST
All

UNIT	CUSTOMER	SALE DATE	AMOUNT	RECEIVED	PENDING	PAYMENT	GST	
A101 Wing A	Nilesh & Rohini Khandelwal 9860112233	2026-08-12	₹72,50,000 incl GST ₹3,62,500	₹72,50,000	—	Paid	GST	Edit
A102 Wing A	Farhan Sheikh 9860223344	—	₹73,20,000 incl GST ₹3,66,000	₹21,96,000	₹51,24,000	Partially Paid	GST	+ Payment Edit
A201 Wing A	Prashant Ambekar 9860556677	—	₹74,15,000 incl GST ₹3,70,750	₹5,00,000	₹69,15,000	Partially Paid	GST	+ Payment Edit

3 records · page 1 of 1

Prev
Next

Unit sales with collections and pending balances

Stat cards (units sold, sale value, received, pending). Sales table with status. **+ New Sale** — cascading **Project→Wing→Floor→Unit (only available units)**, customer details, dates, amount, GST. Row → **payments**: full payment history + **Add Payment**.

5.14 Documents

Construction ERP
Project Tracking System

MAIN

Dashboard
Projects
Daily Progress
Milestones

SITE MANAGEMENT

Drawings
Issues
Inspections
Test Reports
Documents

RESOURCES & COST

Materials
BOQ
Billing & Cost

S
Suresh Deshm...
Super Admin

Documents

Project Documents
+ Upload Document

Search

Title, number, description...

Project

All

Category

All

DOCUMENT	CATEGORY	DOC NO	VER	EXPIRY	FILE	UPLOADED BY	
Commencement Certificate — Wing A-C Sunrise Heights	• Approval	—	—	—	cc-wings.pdf	Amit Verma	Download Delete
Contractor Workmen Compensation Policy Sunrise Heights	• Insurance	—	—	2026-09-10	wc-policy.pdf	Anita Rao	Download Delete
Tower Crane Load Test Certificate Sunrise Heights	• Equipment	—	—	2026-09-18	crane-load-test.pdf	Sunil Pawar	Download Delete
Fire NOC — Provisional Sunrise Heights	• Approval	—	—	2026-12-31	fire-noc.pdf	Amit Verma	Download Delete

Project documents with expiry alerts

Document register: title, category (contract, insurance, license...), project, **expiry date** (expiring-soon highlighted and shown on the dashboard). Upload (PDF/JPG/PNG/DOC/XLS), download, delete, filter by category/project.

5.15 Reports

**Construction ERP**
Project Tracking System

MAIN

 Dashboard

 Projects

 Daily Progress

 Milestones

SITE MANAGEMENT

 Drawings

 Issues

 Inspections

 Test Reports

 Documents

RESOURCES & COST

 Materials

 BOQ

 Billing & Cost

Reports

²

 **Suresh Deshm...**
Super Admin

Reports Center

**Project Progress**
All projects with status, wings and overall progress

**Daily Progress**
Site daily progress entries with labour and location

**Milestones**
Milestone schedule with target and completion dates

**Material Stock**
Current stock position with received/consumed/damaged

**Material Consumption**
Material consumption history by location

**Purchase Orders**
PO register with values and status

**Billing & Cost**
Cost entries with tax, totals and payment status

**BOQ Summary**
BOQ summary with estimated vs actual variance

**Test Reports**
Lab test reports with results and approvals

**Inspection Reports**
Site inspection register

**Issues**
Issue register with priority and status

**Worker Attendance**
Worker attendance with wages and OT

**Sales**
Unit sales register with collections

**Budget vs Actual**
Project budget vs actual cost with variance %

**Pending Collections**
Outstanding customer payments

**Labour Payments**
Labour payment register

Reports centre — 17 one-click reports

**Construction ERP**
Project Tracking System

MAIN

 Dashboard

 Projects

 Daily Progress

 Milestones

SITE MANAGEMENT

 Drawings

 Issues

 Inspections

 Test Reports

 Documents

RESOURCES & COST

 Materials

 BOQ

 Billing & Cost

Reports

²

 **Suresh Deshm...**
Super Admin

Budget vs Actual

From
mm/dd/yyyy

To
mm/dd/yyyy

 Export CSV / Excel

 Print / PDF

CODE	NAME	BUDGET	ACTUAL COST	VARIANCE	USED PERCENT
PRJ-000001	Sunrise Heights	485000000	125400000	359600000	25.86
PRJ-000002	Tech Park — Phase 2	620000000	2100000	617900000	0.34

Report viewer with date filter, CSV export and print/PDF

Construction ERP v1.0 - Project Tracking System

Page 25

16 report cards: pick one → viewer with date/project filters, on-screen table, **Download CSV**, print. Reports: Project Progress, Daily Progress, Milestones, Material Stock, Material Consumption, Purchase Orders, Billing & Cost, BOQ Summary, Test Reports, Inspection Reports, Issues, Worker Attendance, Sales, Budget vs Actual, Pending Collections, Labour Payments.

5.16 My Profile

Construction ERP
Project Tracking System

My Profile

Suresh Deshmukh
admin@constructionerp.com · EMP-001

• Super Admin • **SUPER ADMIN**

Full name
Suresh Deshmukh

Phone
9822001100

Save profile

As Super Admin you have access to all projects and modules.

Change Password

Current password

New password (min 8 chars)

Confirm new password


Change password


My profile and change password

Edit name/phone, change password; see your roles and project access.

6. Admin Panel — screen guide

6.1 Admin Dashboard

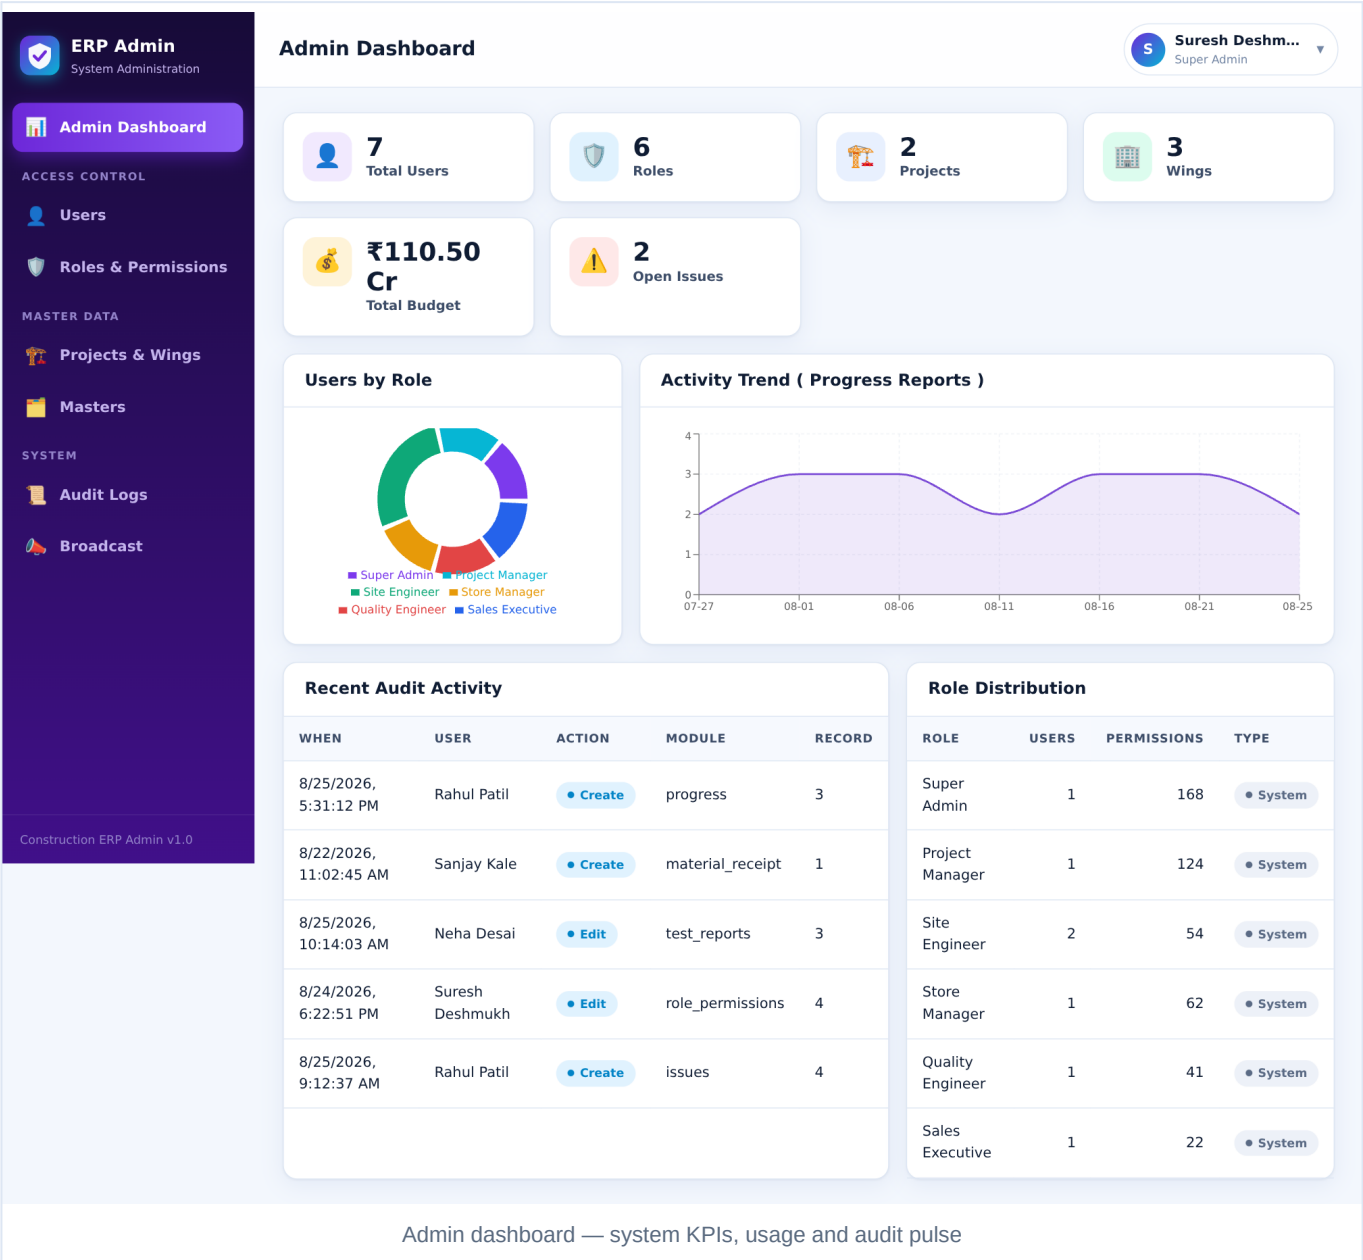

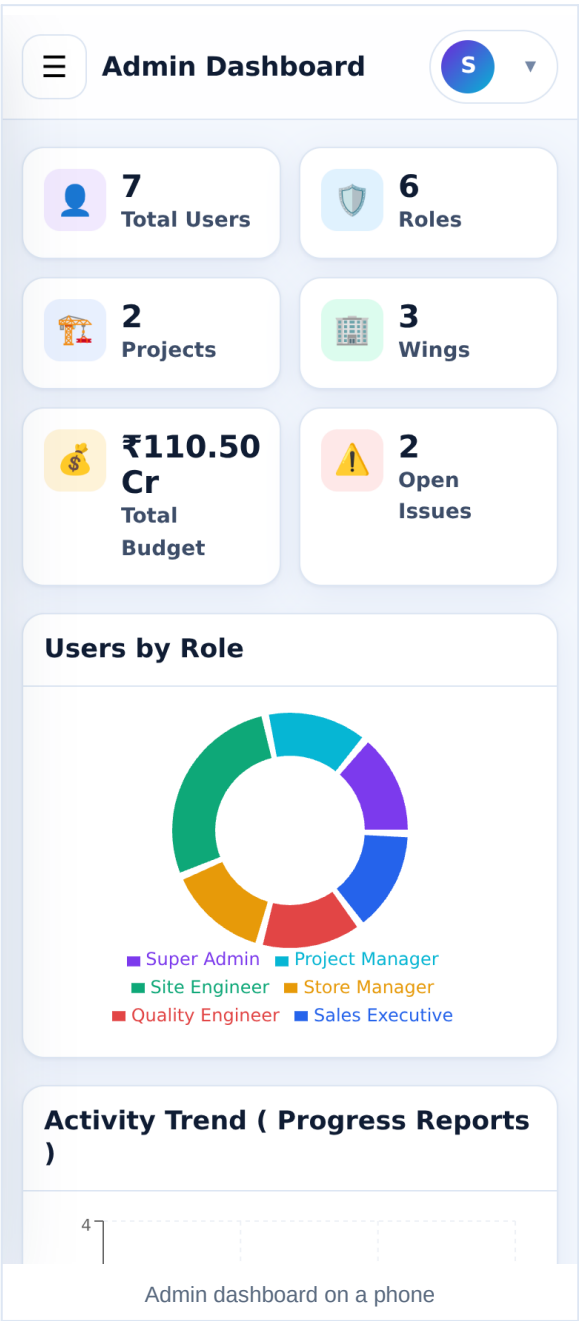

Admin dashboard on a phone

Users by role donut, activity trend, total users/projects/roles/audit count cards, recent audit log table, role list with user counts.

6.2 Users

ERP Admin
System Administration

Admin Dashboard

ACCESS CONTROL

Users

Roles & Permissions

MASTER DATA

Projects & Wings

Masters

SYSTEM

Audit Logs

Broadcast

Construction ERP Admin v1.0

User Management

Suresh Deshm...
Super Admin

Users

↓ Export
+ New User

Search
Name, email, code, phone...

Role
All roles

USER	CODE	PHONE	ROLES	LAST LOGIN	STATUS	
S Suresh Deshmukh admin@constructionerp.com	EMP-001	9822001100	• —	never	• Active	Edit Reset PW
A Amit Verma pm@constructionerp.com	EMP-002	9822011223	• —	never	• Active	Edit Reset PW Delete
R Rahul Patil engineer@constructionerp.com	EMP-003	9822033445	• —	never	• Active	Edit Reset PW Delete
V Vikram Joshi electrical@constructionerp.com	EMP-006	9822055667	• —	never	• Active	Edit Reset PW Delete
S Sanjay Kale store@constructionerp.com	EMP-008	9822077889	• —	never	• Active	Edit Reset PW Delete
N Neha Desai quality@constructionerp.com	EMP-011	9822099001	• —	never	• Active	Edit Reset PW Delete
K Kavita Menon sales@constructionerp.com	EMP-009	9822001122	• —	never	• Active	Edit Reset PW Delete

7 records · page 1 of 1
< Prev
Next >

User management with roles and project access

All users (search, filter by status/role). **+ New User** (account details). Row actions: **Edit**, **Roles** (toggle role chips), **Project Access** (rows of project + optional wing restriction — this is how wing-scoped engineers are configured), **Reset Password** (set a new password directly), **Enable/Disable**, **Delete**. Export users to CSV.

6.3 Roles & Permission Matrix

**ERP Admin**
System Administration

Admin Dashboard

ACCESS CONTROL

Users

**Roles & Permissions**

MASTER DATA

Projects & Wings

Masters

SYSTEM

Audit Logs

Broadcast

Construction ERP Admin v1.0

Roles & Permissions

S Suresh Deshm...
Super Admin

+ New Role

ROLE	DESCRIPTION	USERS	PERMISSIONS	TYPE	STATUS	
Super Admin super_admin	Full system access	1	168	System	Inactive	
Project Manager project_manager	Owens assigned projects end-to-end	1	124	System	Inactive	Permissions
Site Engineer site_engineer	Progress, attendance, issues on site	2	54	System	Inactive	Permissions
Store Manager store_manager	Materials, POs, stock	1	62	System	Inactive	Permissions
Quality Engineer quality_engineer	Test reports & inspections	1	41	System	Inactive	Permissions
Sales Executive sales_executive	Unit sales & collections	1	22	System	Inactive	Permissions

Roles with user and permission counts

**ERP Admin**
System Administration

Admin Dashboard

ACCESS CONTROL

Users

**Roles & Permissions**

MASTER DATA

Projects & Wings

Masters

SYSTEM

Audit Logs

Broadcast

Construction ERP Admin v1.0

Permissions — Project Manager

×

MODULE	VIEW	CREATE	EDIT	DELETE	APPROVE	EXPORT	UPLOAD	DOWNLOAD
Dashboard	☒	☒	☒	☐	☒	☐	☐	☐
Projects	☒	☒	☐	☐	☒	☒	☐	☐
Wings	☐	☐	☐	☐	☐	☐	☐	☐
Floors	☐	☐	☐	☐	☐	☐	☐	☐
Units	☒	☒	☒	☒	☐	☐	☐	☐
Progress	☒	☒	☐	☐	☐	☐	☐	☐
Milestones	☐	☐	☐	☐	☐	☐	☐	☐
Drawings	☐	☐	☐	☐	☐	☐	☐	☐
Materials	☒	☒	☐	☐	☐	☐	☐	☐

24 of 168 granted

Cancel

Save permissions

Permission matrix — module × action checkboxes

Role list with user & permission counts. + **New Role** for custom roles. Click **Permissions** on a role → the **matrix editor**: every module (projects, progress, materials, ...) × 8 actions (view/create/edit/delete/approve/export/upload/download) with checkboxes, module-level toggle, live selected count → **Save**.

6.4 Masters

The screenshot displays the ERP Admin interface. On the left is a dark purple sidebar with navigation links: ERP Admin (System Administration), Admin Dashboard, ACCESS CONTROL (Users, Roles & Permissions), MASTER DATA (Projects & Wings, Masters), and SYSTEM (Audit Logs, Broadcast). The 'Masters' link is highlighted. The main content area is titled 'Master Data' and features a horizontal tab bar with 'Material Categories' (selected), Labour Categories, Labour Rates, Contractors, BOQ Categories, Test Types, and Inspection Types. Below the tabs, the 'Material Categories' section includes a '+ New' button and a search bar. A table lists five categories: Steel, Cement, Aggregates, Masonry, and Finishing. Each row shows the category name, description, type (Non-consumable), and an active status (indicated by a red minus icon). Edit and Delete buttons are provided for each category. At the bottom right of the table, it shows '5 records · page 1 of 1' with 'Prev' and 'Next' navigation buttons. A footer bar at the bottom of the main content area reads 'Master data — materials, categories, labour rates and more'.

NAME	DESCRIPTION	TYPE	ACTIVE		
Steel	TMT & structural steel	Non-consumable	⊖	Edit	Delete
Cement	OPC/PPC bags	Non-consumable	⊖	Edit	Delete
Aggregates	Sand, aggregate, grit	Non-consumable	⊖	Edit	Delete
Masonry	Blocks & bricks	Non-consumable	⊖	Edit	Delete
Finishing	Paints, putty, tiles	Non-consumable	⊖	Edit	Delete

5 records · page 1 of 1 < Prev Next >

Master data — materials, categories, labour rates and more

Nine master-data tabs feeding all dropdowns: **Material Categories, Worker Categories, Labour Rates, Contractors, BOQ Categories, Test Types, Inspection Types, Issue Categories, Notification Settings** (enable/disable per event like `issue_assigned`, `low_stock`, `document_expiring`). Full CRUD with activate/deactivate.

6.5 Projects Overview

 **ERP Admin**
System Administration

 **Admin Dashboard**

ACCESS CONTROL

 **Users**

 **Roles & Permissions**

MASTER DATA

 **Projects & Wings**

 **Masters**

SYSTEM

 **Audit Logs**

 **Broadcast**

Construction ERP Admin v1.0

Projects & Wings

S **Suresh Deshm...**
Super Admin

Projects (2)

CODE	PROJECT	CITY	WINGS	STATUS	PROGRESS	BUDGET	MANAGER
PRJ-000001	Sunrise Heights	Nagpur	—	In Progress	38%	₹48,50,00,000	Amit Verma
PRJ-000002	Tech Park — Phase 2	Nagpur	—	Planning	2%	₹62,00,00,000	Amit Verma

All projects with budgets and status

Read-only bird's-eye: all projects, expand a row → its wings → floors with progress — a quick audit of structures without edit rights.

6.6 Audit Logs

**ERP Admin**
System Administration

**Admin Dashboard**

ACCESS CONTROL

**Users**

**Roles & Permissions**

MASTER DATA

**Projects & Wings**

**Masters**

SYSTEM

**Audit Logs**

**Broadcast**

Audit Logs

S

Suresh Deshm...

Super Admin

↓ Export

Search

User or record id...

Module

All

User

All users

WHEN	USER	ACTION	MODULE	RECORD	IP
8/25/2026, 5:31:12 PM	Rahul Patil	Create	progress	3	103.122.x.x
8/22/2026, 11:02:45 AM	Sanjay Kale	Create	material_receipt	1	103.122.x.x
8/25/2026, 10:14:03 AM	Neha Desai	Edit	test_reports	3	103.122.x.x
8/24/2026, 6:22:51 PM	Suresh Deshmukh	Edit	role_permissions	4	10.0.0.8
8/25/2026, 9:12:37 AM	Rahul Patil	Create	issues	4	103.122.x.x

412 records · page 1 of 14

< Prev

Next >

Audit logs — every create/edit/delete with user and time

Complete trail: user, action (create/edit/delete/login...), module, record, **old vs new values (JSON diff view)**, IP, timestamp. Filter by user/module/action/date; export CSV.

6.7 Broadcast

The screenshot shows the 'Broadcast Notification' interface. On the left is a dark purple sidebar with navigation links: ERP Admin (System Administration), Admin Dashboard, ACCESS CONTROL (Users, Roles & Permissions), MASTER DATA (Projects & Wings, Masters), and SYSTEM (Audit Logs, Broadcast). The main content area is titled 'Broadcast Notification' and contains a form with fields for Title, Message, and Type (set to 'Info'). There is a checkbox for 'Send to all active users' and a 'Send broadcast' button. To the right is a 'Preview' section showing a notification card with the title 'Notification title' and the body 'Your message preview appears here...'. At the bottom of the main area, a text label reads 'Broadcast a notification to all or filtered users'.

Compose an in-app + push message: title, body, type. Target **all users**, a role, or hand-picked users (multi-select). Preview before sending.

7. Mobile App — screen guide

Screenshots: run the app through Expo Go on your phone (see §3.1 of the README) and take captures on-device — the web portal captures in §5 also show how every screen adapts to phone widths.

The mobile app mirrors the essentials for site work. Bottom tabs: **Home · Progress · Attendance · Issues · More** (More shows an orange badge when offline items are queued).

7.1 Login

Brand screen → email + password → **Sign In**. Stays signed in (secure token storage, automatic refresh).

7.2 Home (Dashboard)

Greeting + date, stat tiles (projects, avg progress, open issues, pending inspections, low stock, today's attendance), quick-action shortcuts, recent progress & open-issue cards. Tap notifications  to see the latest.

7.3 Progress — list

Project filter chips → report cards (date, %, description, wing/floor, photo count, GPS indicator). Tap a card → **Progress Detail** (full report + photo grid with per-photo GPS/time, map links).

7.4 Progress — capture ("+ New Report")

The flagship screen:

1. **Pick project** (wing/floor optional), date/time auto-filled.
2. **Take photos** with the camera (or attach from gallery) — thumbnails show in a strip; each photo stores **GPS position + capture time**.

3. Fill work description, % complete, labour count, material used, weather, remarks.
4. **Submit** — uploads photos + metadata; if offline, it saves to the **Sync Queue** instead (duplicate-protected by a client reference).

7.5 Attendance

Date (default today) + project/wing → the worker list; quick-mark icons: **P / A / L / H / OT** per worker, OT hours stepper; header shows running day cost; **Mark all present** button; **Save** posts the entire grid in one call (idempotent re-saves allowed for corrections).

7.6 Issues

List with status/priority filters. ■ **Raise Issue**: camera photos + GPS, title, category, priority, location notes, assign to a teammate, due date — works offline too and queues. Detail screen: status timeline, actions (assign/start/resolve/close/reopen) and comments with author/time.

7.7 Inspections

Under **More** → **Inspections**: list; open one → the checklist: tap **pass/fail/N/A** per item + remarks, add notes, and submit status — inspection updates sync to the same backend tables as the web portal.

7.8 More

- **Offline Sync** — queue of pending progress/issues with per-item status; **Sync now** retries immediately; auto-sync runs when connectivity returns.
- **Notifications** — full notification list (assignments, approvals, alerts).
- **Profile & sync status**, app info, **Logout**.

Push notifications: on first login the app asks permission and registers your device — you then receive push alerts (issue assignments, approvals, broadcasts).

8. A day in the life, by role

Site Engineer — 8:30 AM mark attendance (mobile) → through the day: raise issues as spotted (photo), consume materials (web/app) → 5:30 PM submit daily progress with photos + % → check Sync queue shows 0 pending.

Project Manager — Morning dashboard (issues, low stock, attendance) → approve material requirements & BOQ changes → review yesterday's progress % per wing → update milestones, weekly reports to management (CSV export).

Store Manager — Check **Stock & Alerts** → run low-stock list → create requirements → convert approved ones to POs → record GRNs on delivery → reconcile consumption entries.

Quality Engineer — Book today's inspection (checklist on mobile) → upload lab test report PDFs with results → approve/reject pending test reports → raise issues from failures.

Accountant — Book vendor invoices in Billing → generate labour payments from attendance → record sales receipts in Sales → export Pending Collections + Budget vs Actual for the review meeting.

Admin — Add new joiners & assign roles/project access → check Audit logs → broadcast safety notices.

9. Status & workflow reference

Entity	Statuses
Project	planning → in_progress → on_hold / completed / cancelled
Wing/Floor	planning → in_progress → completed
Milestone	pending → in_progress → completed (auto delayed past target)
Requirement	pending → approved → po_created (or rejected)

Entity	Statuses
Purchase Order	draft → sent → partially_received → completed (or cancelled)
Test Report	pending → pass / fail / inconclusive
Inspection	pending → passed / failed / reinspection_required → closed
Issue	open → assigned → in_progress → resolved → closed (reopened anytime) — priorities low/medium/high/critical
Attendance	present / absent / leave / half_day / overtime
Labour payment	pending → partial → paid
Cost entry	unpaid → partial → paid
Sale	pending → partially_paid → paid (overdue)
Sale unit	available → booked → sold
Document	active → expiring (30-day watch) → expired

Photo/file formats: JPG, JPEG, PNG, WEBP, PDF, XLS, XLSX, DOC, DOCX (max 20 MB per file by default). **Every uploaded file requires login + project access** to view.

10. Tips, FAQ & troubleshooting

Tips

- Attach photos **at the site** — GPS is captured automatically, giving you tamper-proof location+tamper evidence.
- Use the web portal's filter bars — almost every list filters by project, wing, date range and status before CSV export, so exports are already sliced.
- Can't find a menu item? It's permission-related — ask your admin to check your role in the **permission matrix**.
- Assign engineers to specific **wings** for large projects to keep lists short and access tight.

FAQ

- *I submitted progress twice by mistake* — offline sync uses a client reference, so retries never duplicate; if you created two by hand on web, delete one (editors with delete permission).
- *Why can't I consume material?* — stock is validated live; add a GRN first or reduce the quantity.
- *Why did my milestone turn "delayed"?* — target date passed while status wasn't completed; update the % or the target date.
- *Push notifications not arriving?* — allow notifications when the app asks (or in phone settings), and confirm you're logged in; tokens register on login.
- *GPS shows "unavailable"* — grant the app Location permission (and camera permission for photos) when asked.

Troubleshooting

- *Login fails with "Invalid credentials"* — verify caps lock; use **Forgot password**; admin can also reset it from Admin Panel → Users.
- *"Network error" on mobile at site* — the app works offline: finish entries; they'll sync when you reconnect. For full features, the API server must be reachable at the configured address.
- *Photo won't upload (>20 MB)* — retake at normal resolution or compress; the limit protects site bandwidth.

For installation, see [docs/INSTALLATION.md](#) · for the API, [docs/API.md](#) · for deployment, [docs/DEPLOYMENT.md](#).
